


标识号	0	任务模式	任务名称	工期	开始时间	完成时间	前置任务	资源名称
1		<u>-</u> 5	业务目标确认	2 个工作	2023年5月 8日	2023年5月 9日		
2		<u>_</u>	商业分析			12023年5月1	1	
3		<u>_</u>				12023年5月1		
4		<u>_</u>	场景分析			12023年5月1		
5		<u>_</u>	需求建模			12023年5月2		
6		<del>-</del> 5	数据信息结构设计	3 个工作				
7		<u>-</u>	硬件结构 设计	3 个工作 日	2023年5月 24日	2023年5月 26日	5	
8		<u>-</u> 5	页面信息 结构设计	3 个工作 日	2023年5月 24日	26日	5	
9		<u>_</u>	原型设计	7 个工作日	2023年5月	22023年6月6	6,7,8	
10		<u>-</u> 5	需求评审 /产品需求 文档确认	2 个工作日	2023年6月 7日	2023年6月 8日	9	
11		<u>_</u>	界面评审	2 个工作日	2023年6月	92023年6月1	10	
12		<u>-</u>	硬件设计 评审	2 个工作日	2023年6月 9日		10	
13		<u>-</u>	软件核心 开发和测	30 个工作 日	2023年6月 9日	2023年7月 20日	10	
14		<del>-</del> >	安全模块 软件开发 和测试	14 个工作日	2023年6月 9日	2023年6月 28日	10	
15		<del>-</del> >	健康关怀 模块软件 开发和测	14 个工作日	2023年6月 9日	2023年6月 28日	10	
16		<del>-</del> >	中央控制日子	14 个工作日	2023年6月 13日	2023年6月 30日	11	
17		<u>-</u> 5	手机APP 用户界面 开发和测	日 个工作日	2023年6月 13日	2023年6月30日	11	
18		<u>-</u> 5	家庭物联 网协调器 硬件开发	日 个工作日	2023年6月 13日	2023年6月 30日	12	
19		<del>-</del> 5	中央控制台硬件开	14 个工作 日	2023年6月 13日	2023年6月 30日	12	
20		-\$	手机APP整 合测试调	14 个工作 日	2023年7月 21日	2023年8月 9日	13, 14, 15, 17	
21		<b>-</b> 5	中央控制 台测试	14 个工作日	21日	2023年8月 9日	13, 14, 15, 16	
22		<u>-</u>	家庭物联 网协调器 测试调优	7 个工作日	2023年7月3日	2023年7月 11日	18	



标识号	0	任务模式	任务名称	工期	开始时间	完成时间	前置任务	资源名称
23		<u>-</u> ->	中央控制 台硬件测 试调优	7 个工作日	2023年7月 3日	2023年7月 11日	19	
24		<u>-</u> \$	中央控制 台整合测 试调优	7个工作日	2023年8月10日	2023年8月 18日	21,23	
25		<u>-</u> 5		日 个工作	2023年8月21日	2023年9月 7日	20, 22, 24	
26		<u>-</u> 5	最小可行产品上线		2023年9月 8日	2023年9月 12日	25	
27		<u>-</u> 5	产品上线	日	13日	2023年9月 21日	26	
28		<del>-5</del>	总结用户	日	2023年9月 22日	2023年 11月2日	27	
29		<u>-</u>	运维调度	1095 个工	2023年9月2	2027年12月	27	



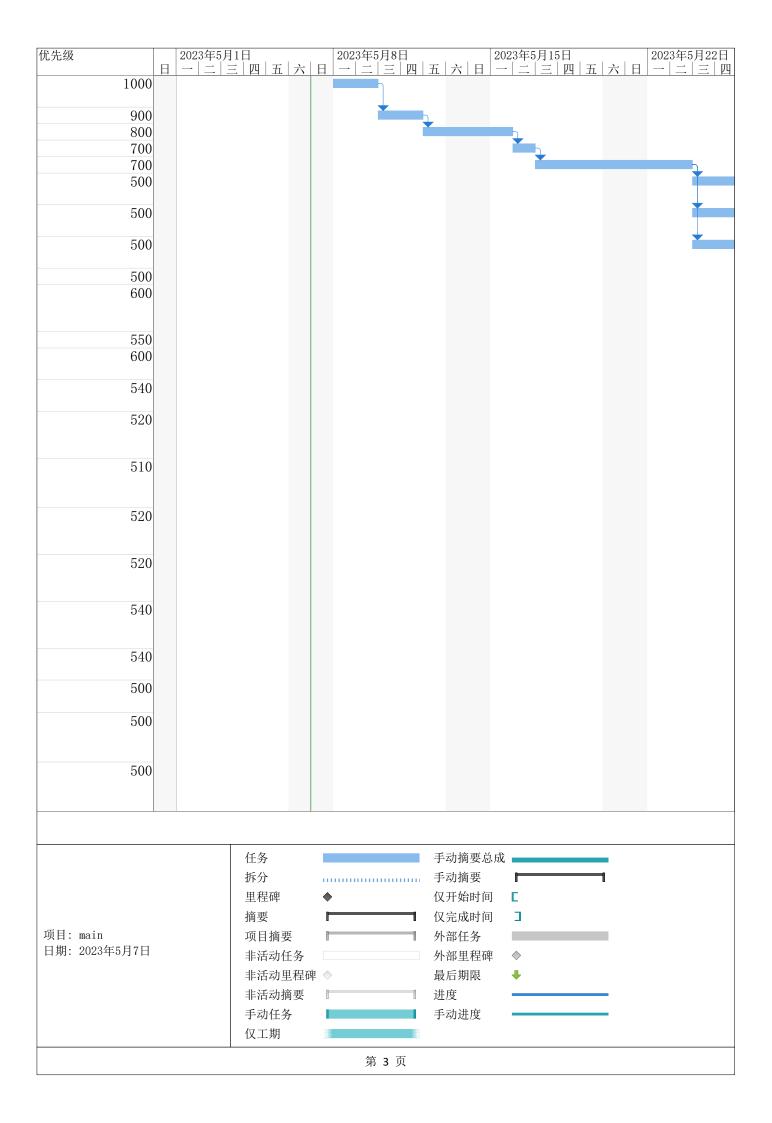

优先级		2023年5月1日		2023年5月8日		2023年5月15日		2023年5月22日
500	日	2023年5月1日   一   二   三   四   五	.   六   E	1   一   二   三   四	五一六日	2023年5月15日 一 二 三 四	五二六日	2023年5月22日  - 二 三 四
300								
500								
500								
500								
600								
600								
000								
480								
500								
500								
		任务			手动摘要总	成		
		拆分			手动摘要			
		里程碑 摘要		<b>♦</b>	仅开始时间			
<b>塔里</b>	项目: main				仅完成时间	]		
项目: main 日期: 2023年5月7日	项目摘!			外部任务	<b>□</b> ♦			
,,		非活动	仕务 里程碑	•	外部里程碑 最后期限	. ♦ <b>.</b>		
		非活动			进度	▼		
		手动任			手动进度			
		仅工期	· •	-				
				<b> </b>				
第 4 页								

